

=====
QUOTE INFORMATION:
=====
Quote Id:
Purchaser:
Project:

Customer Info:

=====
SteelBuildingSupplier.com
225 S Academy Blvd Ste 201
Colorado Springs, CO 80910-2768
(800) 793-8555
Contact:

Quote good for 7 days

=====
BUILDING TYPE
=====
Commercial Rigid Frame Steel

=====
PRICING
=====
Building Components \$

PANEL PACKING 2 sets \$
-----
Subtotal \$
Building Freight \$
Insulation Freight \$
Detail/Draft Fee \$
Stamped Plan Sets ( 1) \$
-----
TOTAL COST \$

SteelBuildingSupplier.com
1-800-793-8555

=====
BUILDING LOCATION
=====
WA 98250

=====
BUILDING DESIGN SPECIFICATIONS
=====

----- Dimensions ----- Loading -----
Width(ft): 44 Wind Code: IBC 00 Exposure: C
Length(ft): 44 Wind (mph): 80 Importance: 1.00
Back eave height(ft): 12 Roof Live Load (psf): 20
Front eave height(ft): 12 Roof Dead Load (psf): 2
Back roof slope: 3.0:12 Roof Snow Load (psf): 21
Front roof slope: 3.0:12 Roof Collateral Load (psf): 1
Seismic: E

Engineering:
Stamped Plan Sets: 1
Design Calc Sets: none

Covering:
Roof: 26 Gauge, PR Panels, Color: NEED COLOR
Sidewall: 26 Gauge, PR Panels, Color: NEED COLOR
Endwall: 26 Gauge, PR Panels, Color: NEED COLOR
Sidewall trim at eave : NEED COLOR
Endwall (rake) trim at roof : NEED COLOR
Outside jamb sheeting trim color: NEED COLOR
Outside corner trim color : NEED COLOR

Framing:
----- Interior -----

1 rigid frame, clear span  
Frame Design Id    Column Type            Rafter Type  
-----  
                  1            tapered depth            tapered depth  
Spacing along front sidewall: 2 at 22

----- Exterior Walls -----

Endwall: Left = Bearing, Bypass girts  
          Right = Bearing, Bypass girts  
Sidewall: Front = Bypass  
          Back = Bypass

----- Wind -----

Roof: Cable Diagonal Bracing  
Endwall: Left = Cable Diagonal Bracing  
          Right = Panel Shear  
Sidewall: Front = Cable Diagonal Bracing  
          Back = Cable Diagonal Bracing

----- Factory Located Framed Openings -----

Factory Located Framed Openings:  
Left Endwall : ( 2 ) 10        W x 10        H  
Front Sidewall : none  
Right Endwall : none  
Back Sidewall : none

Gutters and Downspouts:

Front sidewall gutters(ft): none  
Front sidewall downspouts: none  
Back sidewall gutters(ft): none  
Back sidewall downspouts: none

===== ACCESSORY ITEMS =====

Walk Doors: 1 - 3070MI

Translucent Wall Panels: none

Translucent Roof Panels: none

Liner Panels:


Left Endwall: none  
Right Endwall: none  
Front Sidewall: none  
Back Sidewall: none

Insulation:

Roof: WMP-VR, 2 inch  
Wall: WMP-VR, 2 inch

Delivered Weight: 10877.1 lbs

SteelBuildingSupplier.com  
1-800-793-8555  
Not for construction

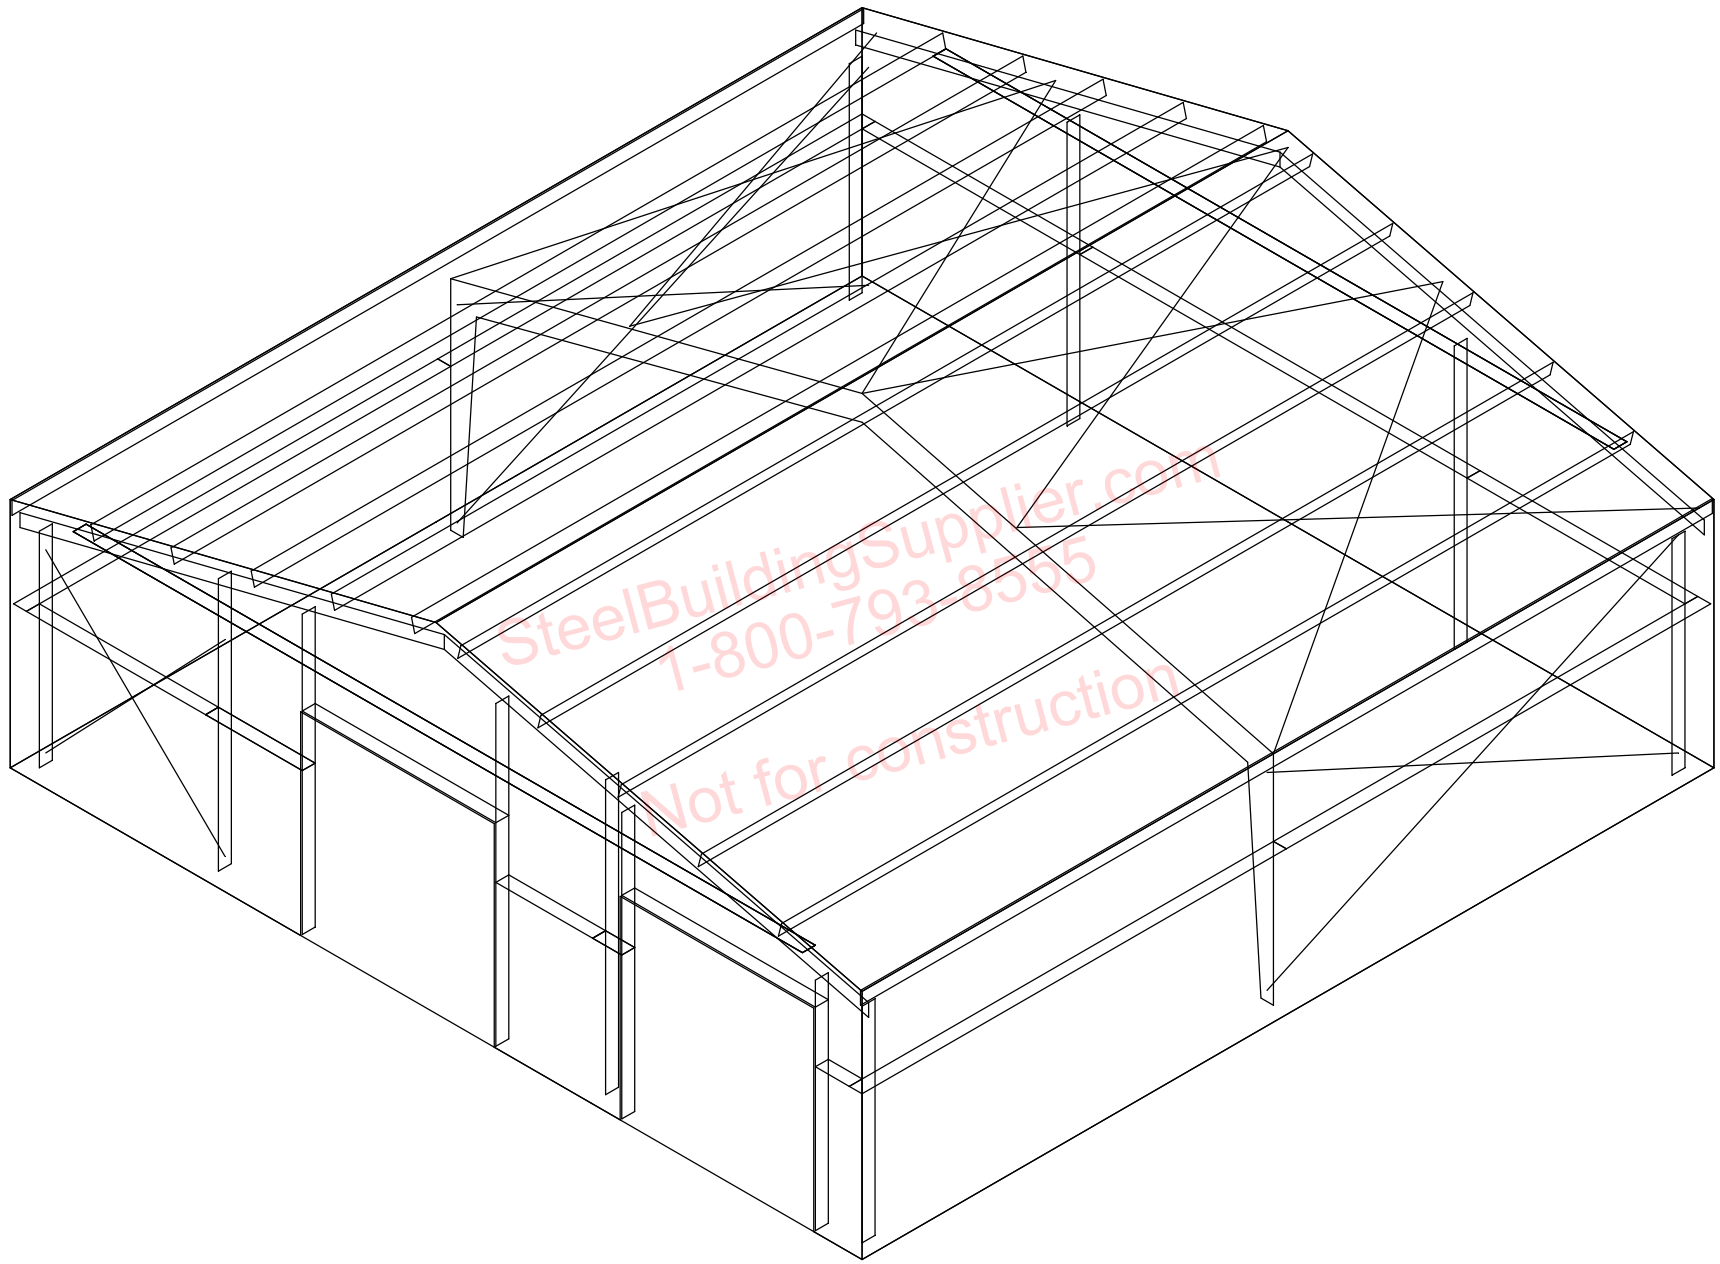

SteelBuildingSupplier.com  
1-800-792-8555


Not for construction

SPLICE BOLTS						
Splice Mark	Quan	Top/Bot/Int	Type	Bolt Dia	Len	-----
SP- 1	4	4	0	A325	5/8"	2'
SP- 2	4	4	0	A325	5/8"	2'

BASE PLATES			
Col Id	Plate Size	Wid	Thick Length
BP- 1	8' 1/2"	8'	1/2"

PIECE	MEMBER SIZE TABLE		OUTSIDE FLANGE W x T x LEN	INSIDE FLANGE W x T x LEN
	WEB DEPTH START/END	WEB PLATE THICK LENGTH		
RF1-1	16.0/16.0	1'-7 1/2"	5x1/4" x1'-4 11/16"	5x5/16"x10'-1 5/8"
RF1-2	7.7/16.0	10'-1 3/8"	5x1/4" x11'-4 13/16"	5x1/4" x20'-5 1/4"
RF1-3	15.1/15.0	2'-0"	5x1/4" x20'-5 1/4"	5x1/4" x20'-5 1/2"
	16.0/15.1	18'-9 5/16"		
	15.1/15.0	2'-0"		
	16.0/15.1	18'-9 5/16"		

▽ FLANGE BRACES: Both Sides (Unless Noted)  
 FBxxA(1): xx=length(in)  
 A - L2X2X14G

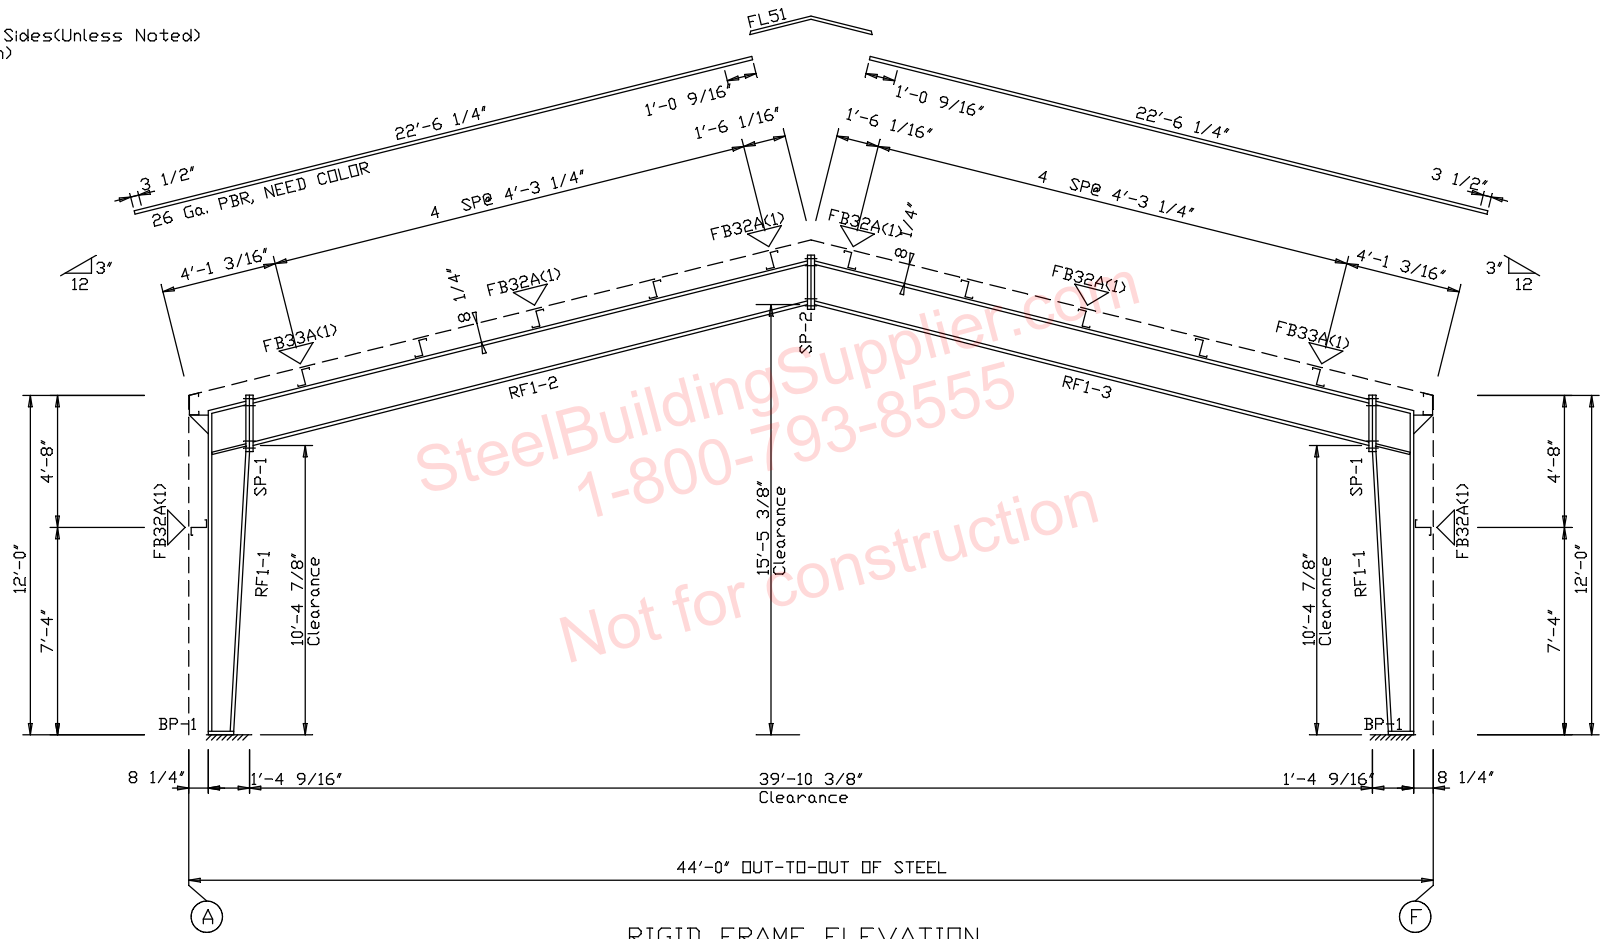


RIGID FRAME ELEVATION  
FOR FRAME LINE 2

SteelBuildingSupplier.com		RIGID FRAME ELEVATION	
PROJECT		DESIGN:	
ID		CHECK:	MBC
PROJECT ADDRESS	Jobsite address Jobsite address 2	DATE:	SHEET OF

ANCHOR BOLT SUMMARY



Qty	Loc	Dia (in)	Proj (in)
8	DJ	3/4"	2.50
8	FW	3/4"	2.50
8	WB	7/8"	3.00

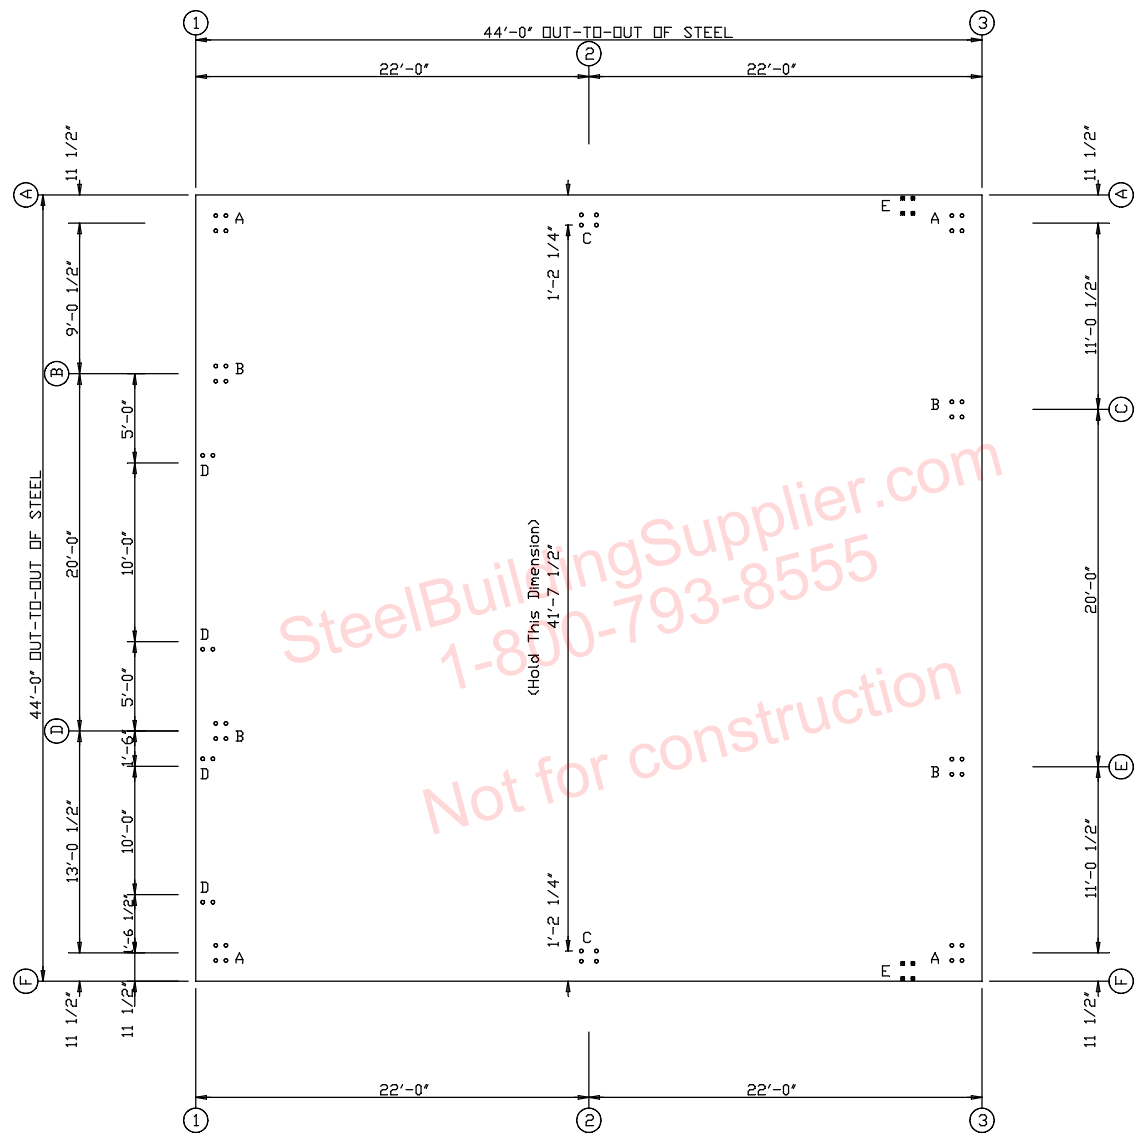

ANCHOR BOLT PLAN  
 NOTE: All Base Plates @ 100'-0" (U.N.)

- Dia= 3/4"
- Dia= 7/8"

SteelBuildingSupplier.com		ANCHOR BOLT PLAN	
PROJECT		DESIGN:	
ID		CHECK:	MBC
PROJECT ADDRESS	Jobsite address Jobsite address 2	DATE:	SHEET OF

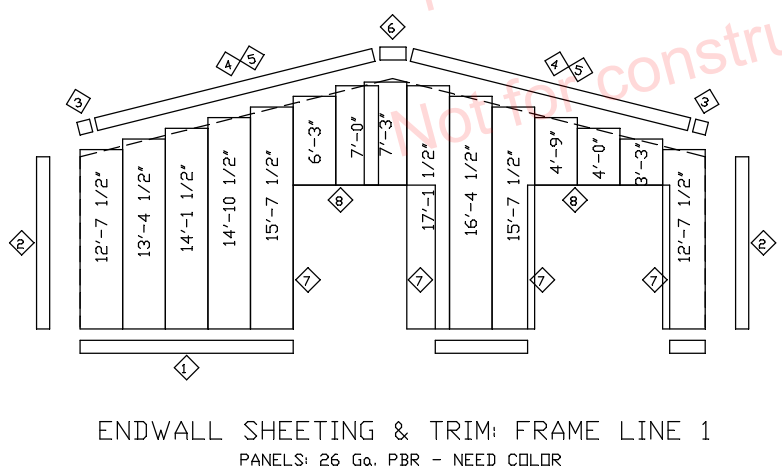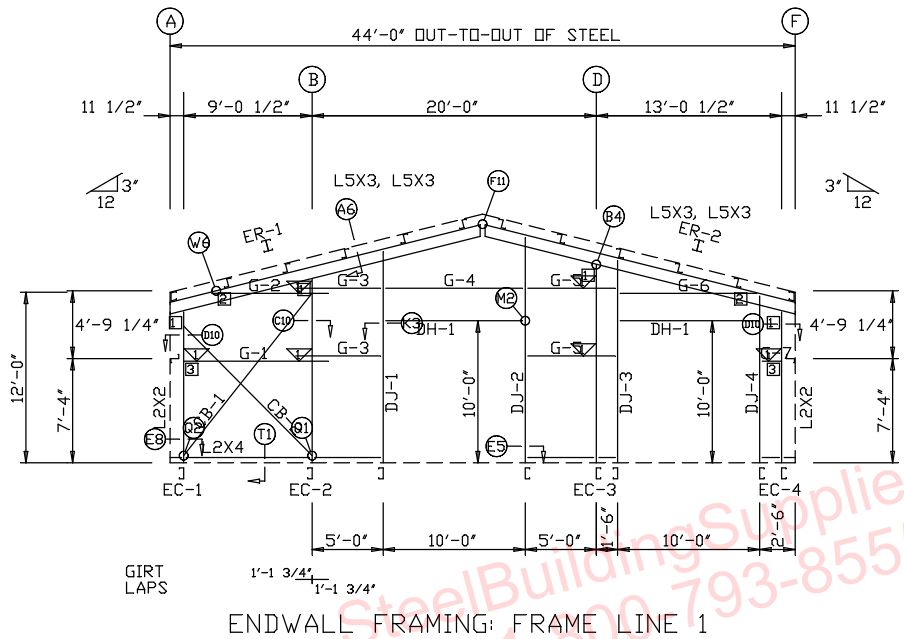

BOLT TABLE				
FRAME LINE 1				
LOCATION	QUAN	TYPE	DIA	LENGTH
ER-1/ER-2	4	A325	5/8"	2"
Columns	4	A325	5/8"	2"
Jamb	2	A325	5/8"	2"

MEMBER TABLE		
FRAME LINE 1		
MARK	PART	LENGTH
EC-1		10'-9 1/16"
EC-2		13'-0 3/16"
EC-3		14'-0 3/16"
EC-4		10'-9 1/16"
ER-1		22'-7 7/8"
ER-2		22'-7 7/8"
DJ-1		15'-0 1/4"
DJ-2		16'-0 1/4"
DJ-3		14'-5 5/8"
DJ-4		11'-10 3/4"
DH-1		10'-0"
G-1		10'-2 1/4"
G-2		7'-10 3/4"
G-3		5'-9 3/4"
G-4		9'-3 1/2"
G-5		5'-10"
G-6		8'-10 3/4"
G-7		1'-2 1/2"
CB-1	1/2" Cable	15'-8"
CB-2	1/2" Cable	13'-11"

TRIM TABLE		
FRAME LINE 1		
ID	PART	LENGTH
1	FL-72	10'-2"
2	FL-831	12'-0"
3	FL-13A	2"
4	FL-13	10'-2"
5	FL-13D	20'-2"
6	FL-13C	1'-4"
7	FL-23	10'-2"
8	FL-26	10'-4"

FLANGE BRACE TABLE		
FRAME LINE 1		
ID	MARK	LENGTH
1	FB31	2'-7"

CONNECTION PLATES	
FRAME LINE 1	
ID	MARK/PART
1	BOLT
2	c1
3	SC-5

SteelBuildingSupplier.com		
PROJECT		ENDWALL FRAMING
ID		DESIGN:
PROJECT ADDRESS	Jobsite address	CHECK:
	Jobsite address 2	DATE:
		SHEET
		OF
